

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

**Improvements to Kings Highway (C.R. 551-S) from Market Street
(C.R. 634, MP 1.23) to Hopkins Road (C.R. 647, MP 3.65)
*Bid No. B6-24***

*Boroughs of Mount Ephraim, Audubon, and Haddon Heights
Camden County, New Jersey*

CED Project No. 24001861G

Progress Report #2

Monday, September 30, 2024, to Friday, October 04, 2024



Figure:1

*Rubblization of West Bound concrete roadway pavement using
a Multi-Head Breaking (MBH) Equipment.*

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



*Figure 2:
Partial depth repairs of deteriorating/spalling concrete pavement at various locations.*



*Figure 3:
Milling and temporary paving operations of East Bound shoulder
between East Lake Drive to West Atlantic Ave.*

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

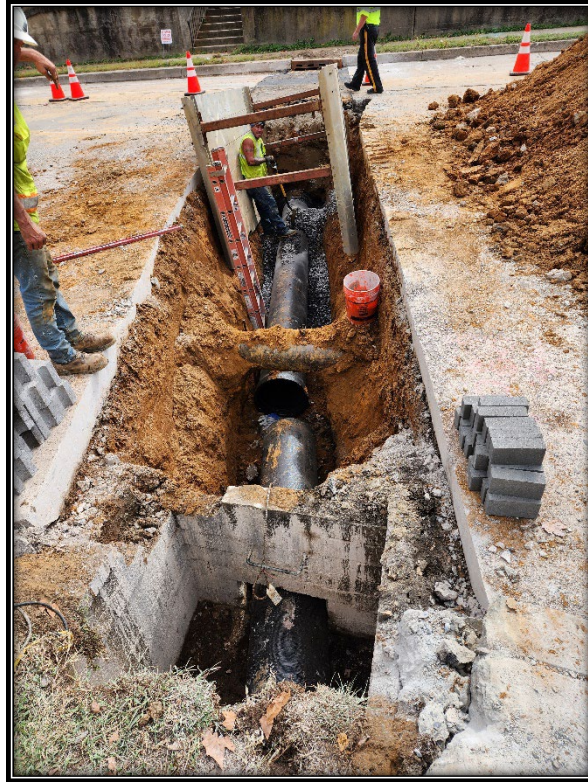


Figure 4:

Replacement of 18" ductile iron drainage pipe near the intersection of Hill (STA 35+50), connecting the north and south inlets. In addition, inlet was reconstructed, grate and curb piece were replaced.



Figure 5:

PSE&G began relocating utility poles to accommodate roadway widening.

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



*Figure 6:
Installed inlet filter with new grate.*

- **Work Completed this week:**

- Rubblization of concrete pavement at West Bound Shoulder between Atlantic Ave and Lake Drive.
- Partial depth repairs of concrete pavement at various locations.
- Milling and temporary paving of East Bound shoulder from Atlantic Ave to Lake Drive.
- Replaced 18" iron ductile drainage pipes at 35+50.
- Reconstruction of inlet, replaced drainage grate (with inlet filter) and curb piece at 35+50.

- **Items completed this period:**

- Rubblization of concrete pavement
- Partial repairs
- Replacement of 18" Iron ductile pipe
- Reconstruction of inlet
- Drainage grate replacement
- Curb piece replacement
- Inlet filter installation

- **Progress Next Two Weeks:**

- Mobilization of crews
- Traffic Control Set up

- **Next Progress Meeting:**

- The next Progress Meeting has been scheduled for Tuesday, October 15, 2024, at 2:30 PM.
 - Bid Award Date: July 18, 2024
 - Notice to Proceed: 9/9/24
 - Start Date: 9/9/24
 - Substantial Completion Date: 340 days, August 15, 2025
 - Stop Work: N/A
 - Amended NTP: N/A+
 - Final Completion Date: September 24, 2025
 - Initial Award: \$10,745,085.83

Prepared by: Obed Okeyo
Resident Engineer
Colliers Engineering & Design

James Winckowski, PE, County Engineer
